





Activity ID		Activity Name	Original Duration	Start	Finish	Total Float	Qtr 3, 2013		Qtr 4, 2013		Qtr 1, 2014			Qtr 2, 2014			Qtr 3, 2014			Qtr 4, 2014			Qtr 1, 2015	
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
		<div></div> 1900	1ST.MASONARY SHOPDRAWING SUBMITAL	5	07-Dec-13	14-Dec-13	68					<div></div> 1ST.MASONARY SHOPDRAWING SUBMITAL												
		<div></div> 1910	1ST.MASONARY SHOPDRAWING APPROVAL	5	14-Dec-13	21-Dec-13	68					<div></div> 1ST.MASONARY SHOPDRAWING APPROVAL												
		<div></div> 2nd floor		10	21-Dec-13	06-Jan-14	68					<div></div> 06-Jan-14, 2nd floor												
		<div></div> 1920	2ND.MASONARY SHOPDRAWING SUBMITAL	5	21-Dec-13	29-Dec-13	68					<div></div> 2ND.MASONARY SHOPDRAWING SUBMITAL												
		<div></div> 1930	2ND.MASONARY SHOPDRAWING APPROVAL	5	30-Dec-13	06-Jan-14	68					<div></div> 2ND.MASONARY SHOPDRAWING APPROVAL												
		<div></div> 3rd floor		10	30-Dec-13	13-Jan-14	89					<div></div> 13-Jan-14, 3rd floor												
		<div></div> 1940	3RD.MASONARY SHOPDRAWING SUBMITAL	5	30-Dec-13	06-Jan-14	89					<div></div> 3RD.MASONARY SHOPDRAWING SUBMITAL												
		<div></div> 1950	3RD.MASONARY SHOPDRAWING APPROVAL	5	06-Jan-14	13-Jan-14	89					<div></div> 3RD.MASONARY SHOPDRAWING APPROVAL												
		<div></div> roof floor		10	06-Jan-14	20-Jan-14	113					<div></div> 20-Jan-14, roof floor												
		<div></div> 1960	ROOF MASONARY SHOPDRAWING SUBMITAL	5	06-Jan-14	13-Jan-14	113					<div></div> ROOF MASONARY SHOPDRAWING SUBMITAL												
		<div></div> 1970	ROOF MASONARY SHOPDRAWING APPROVAL	5	13-Jan-14	20-Jan-14	113					<div></div> ROOF MASONARY SHOPDRAWING APPROVAL												
		<div></div> civil material		28	16-Oct-13	26-Nov-13	307					<div></div> 26-Nov-13, civil material												
		<div></div> all floor		28	16-Oct-13	26-Nov-13	307					<div></div> 26-Nov-13, all floor												
		<div></div> 1570	ISOLATION MATERIAL SUBMITAL	5	16-Oct-13	23-Oct-13	330					<div></div> ISOLATION MATERIAL SUBMITAL												
		<div></div> 1580	ISOLATION MATERIAL APPROVAL	5	24-Oct-13	31-Oct-13	310					<div></div> ISOLATION MATERIAL APPROVAL												
		<div></div> 1590	ISOLATION MATERIAL PROCURMENT	5	31-Oct-13	07-Nov-13	310					<div></div> ISOLATION MATERIAL PROCURMENT												
		<div></div> 1600	ISOLATION MATERIAL PROCURMENT	10	07-Nov-13	21-Nov-13	310					<div></div> ISOLATION MATERIAL PROCURMENT												
		<div></div> 1980	backfill MATERIAL SUBMITAL	5	21-Oct-13	28-Oct-13	312					<div></div> backfill MATERIAL SUBMITAL												
		<div></div> 1990	backfill MATERIAL APPROVAL	5	28-Oct-13	04-Nov-13	312					<div></div> backfill MATERIAL APPROVAL												
		<div></div> 2000	backfill MATERIAL PROCURMENT	5	05-Nov-13	12-Nov-13	312					<div></div> backfill MATERIAL PROCURMENT												
		<div></div> 2010	backfill MATERIAL PROCURMENT	10	12-Nov-13	26-Nov-13	307					<div></div> backfill MATERIAL PROCURMENT												
		<div></div> finishing material		286	21-Sep-13	13-Nov-14	67					<div></div> 13-Nov-14, finishing material												
		<div></div> all floor		286	21-Sep-13	13-Nov-14	67					<div></div> 13-Nov-14, all floor												
		<div></div> 1610	BRICK MATERIAL SUBMITAL	5	31-Oct-13	07-Nov-13	310					<div></div> BRICK MATERIAL SUBMITAL												
		<div></div> 1620	BRICK MATERIAL APPROVAL	5	21-Sep-13	28-Sep-13	343					<div></div> BRICK MATERIAL APPROVAL												
		<div></div> 1630	BRICK MATERIAL PROCURMENT	5	28-Sep-13	05-Oct-13	343					<div></div> BRICK MATERIAL PROCURMENT												
		<div></div> 1640	BRICK MATERIAL DELIEVERY	30	05-Oct-13	18-Nov-13	313					<div></div> BRICK MATERIAL DELIEVERY												
		<div></div> 1650	CERMIC MATERIAL SUBMITAL	5	07-Nov-13	14-Nov-13	310					<div></div> CERMIC MATERIAL SUBMITAL												
		<div></div> 1660	CERMIC MATERIAL APPROVAL	5	31-Oct-13	07-Nov-13	320					<div></div> CERMIC MATERIAL APPROVAL												
		<div></div> 1670	CERMIC MATERIAL PROCURMENT	5	07-Nov-13	14-Nov-13	315					<div></div> CERMIC MATERIAL PROCURMENT												
		<div></div> 1680	CERMIC MATERIAL DELIEVERY	60	14-Nov-13	12-Feb-14	255					<div></div> CERMIC MATERIAL DELIEVERY												
		<div></div> 1690	RED TILES MATERIAL SUBMITAL	5	01-Oct-14	08-Oct-14	92					<div></div> RED TILES MATERIAL SUBMITAL												
		<div></div> 1700	RED TILES MATERIAL APPROVAL	5	08-Oct-14	15-Oct-14	87					<div></div> RED TILES MATERIAL APPROVAL												
		<div></div> 1710	RED TILES MATERIAL PROCURMENT	5	15-Oct-14	22-Oct-14	82					<div></div> RED TILES MATERIAL PROCURMENT												
		<div></div> 1720	RED TILES MATERIAL DELIEVERY	15	23-Oct-14	13-Nov-14	67					<div></div> RED TILES MATERIAL DELIEVERY												
		<div></div> substructure		56	16-Sep-13	08-Dec-13	0					<div></div> 08-Dec-13, substructure												
		<div></div> earthwork		54	16-Sep-13	04-Dec-13	0					<div></div> 04-Dec-13, earthwork												
		<div></div> underground		54	16-Sep-13	04-Dec-13	0					<div></div> 04-Dec-13, underground												
		<div></div> 10	EXCAVATION	10	16-Sep-13	30-Sep-13	0					<div></div> EXCAVATION												
		<div></div> 20	REPLACMENT LAYER	7	01-Oct-13	10-Oct-13	0					<div></div> REPLACMENT LAYER												
<div></div> 30	BACKFILL	5	26-Nov-13	04-Dec-13	0					<div></div> BACKFILL														
<div></div> concrete work		39	10-Oct-13	08-Dec-13	0					<div></div> 08-Dec-13, concrete work														
<div></div> underground		39	10-Oct-13	08-Dec-13	0					<div></div> 08-Dec-13, underground														
<div></div> 40	P.C	7	10-Oct-13	21-Oct-13	0					<div></div> P.C														
<div></div> 50	R.C	12	21-Oct-13	07-Nov-13	0					<div></div> R.C														
<div></div> 60	NECK COLUMN	7	07-Nov-13	18-Nov-13	0					<div></div> NECK COLUMN														
<div></div> 70	SLAB ON GRADE	2	05-Dec-13	08-Dec-13	0					<div></div> SLAB ON GRADE														
<div></div> masonry		3	18-Nov-13	21-Nov-13	0					<div></div> 21-Nov-13, masorlary														
<div></div> underground		3	18-Nov-13	21-Nov-13	0					<div></div> 21-Nov-13, underground														
<div></div> 100	BRICK WORK	3	18-Nov-13	21-Nov-13	0					<div></div> BRICK WORK														
<div></div> thermal		3	23-Nov-13	26-Nov-13	0					<div></div> 26-Nov-13, thermal														



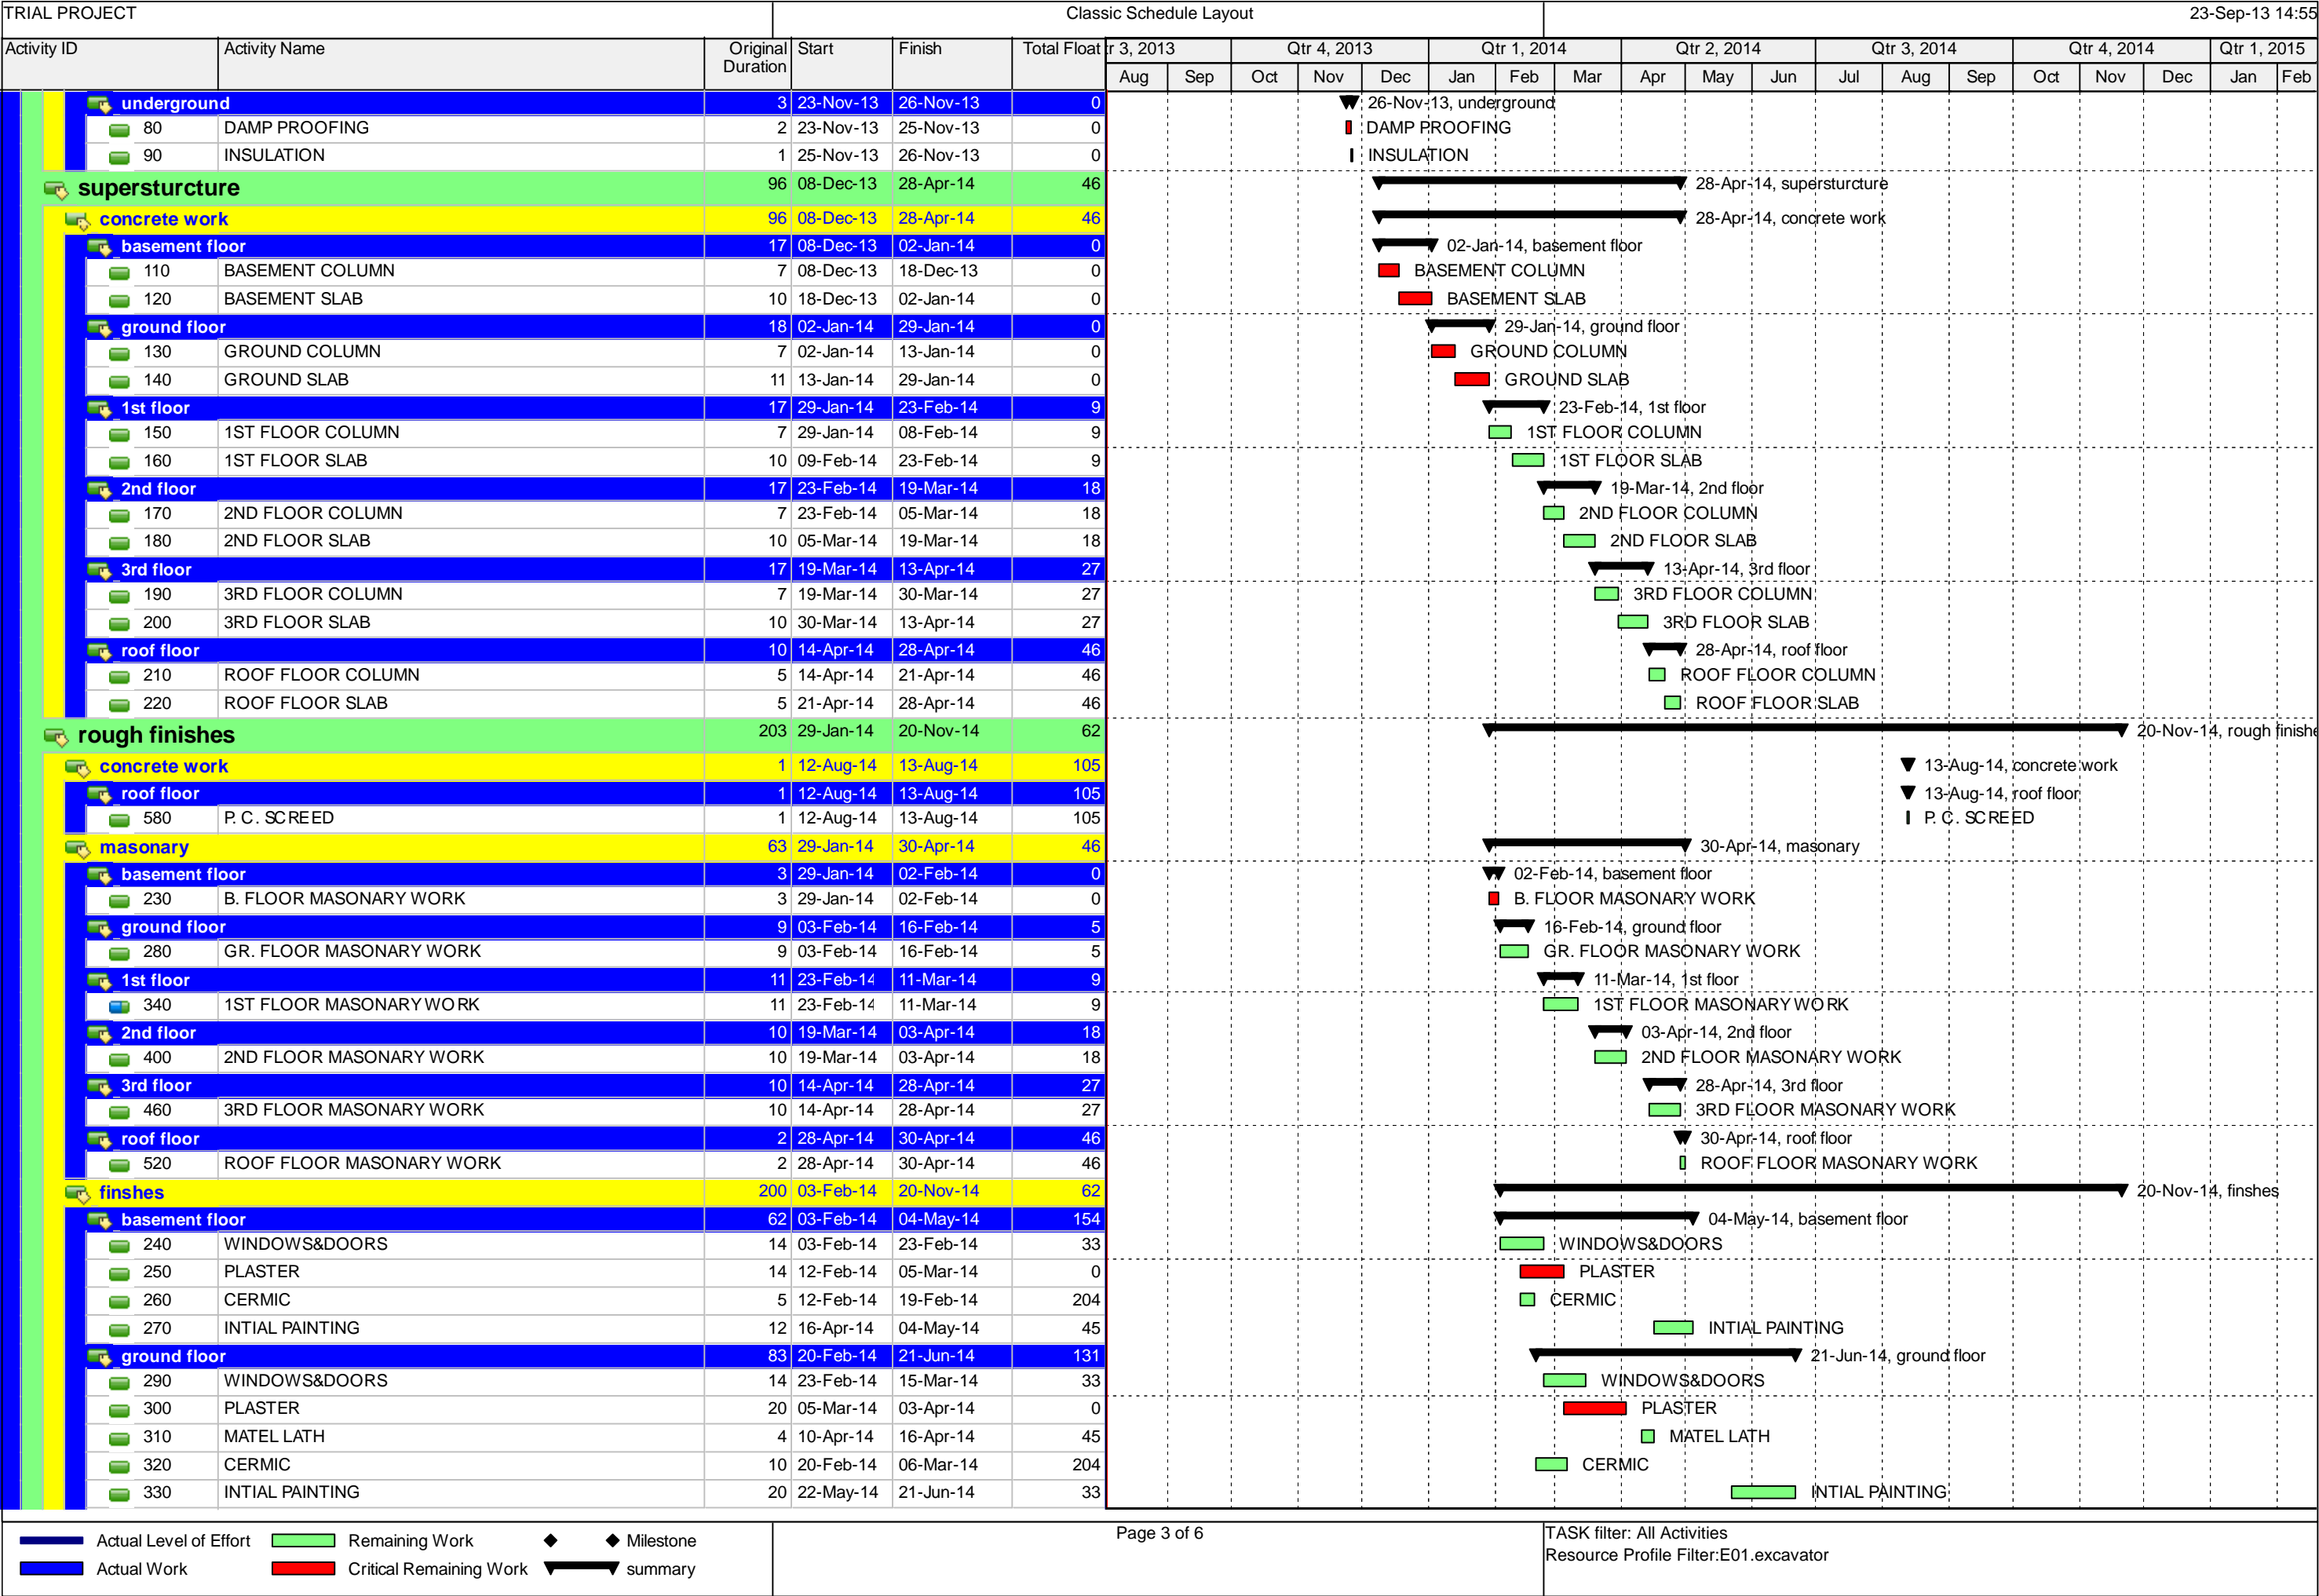

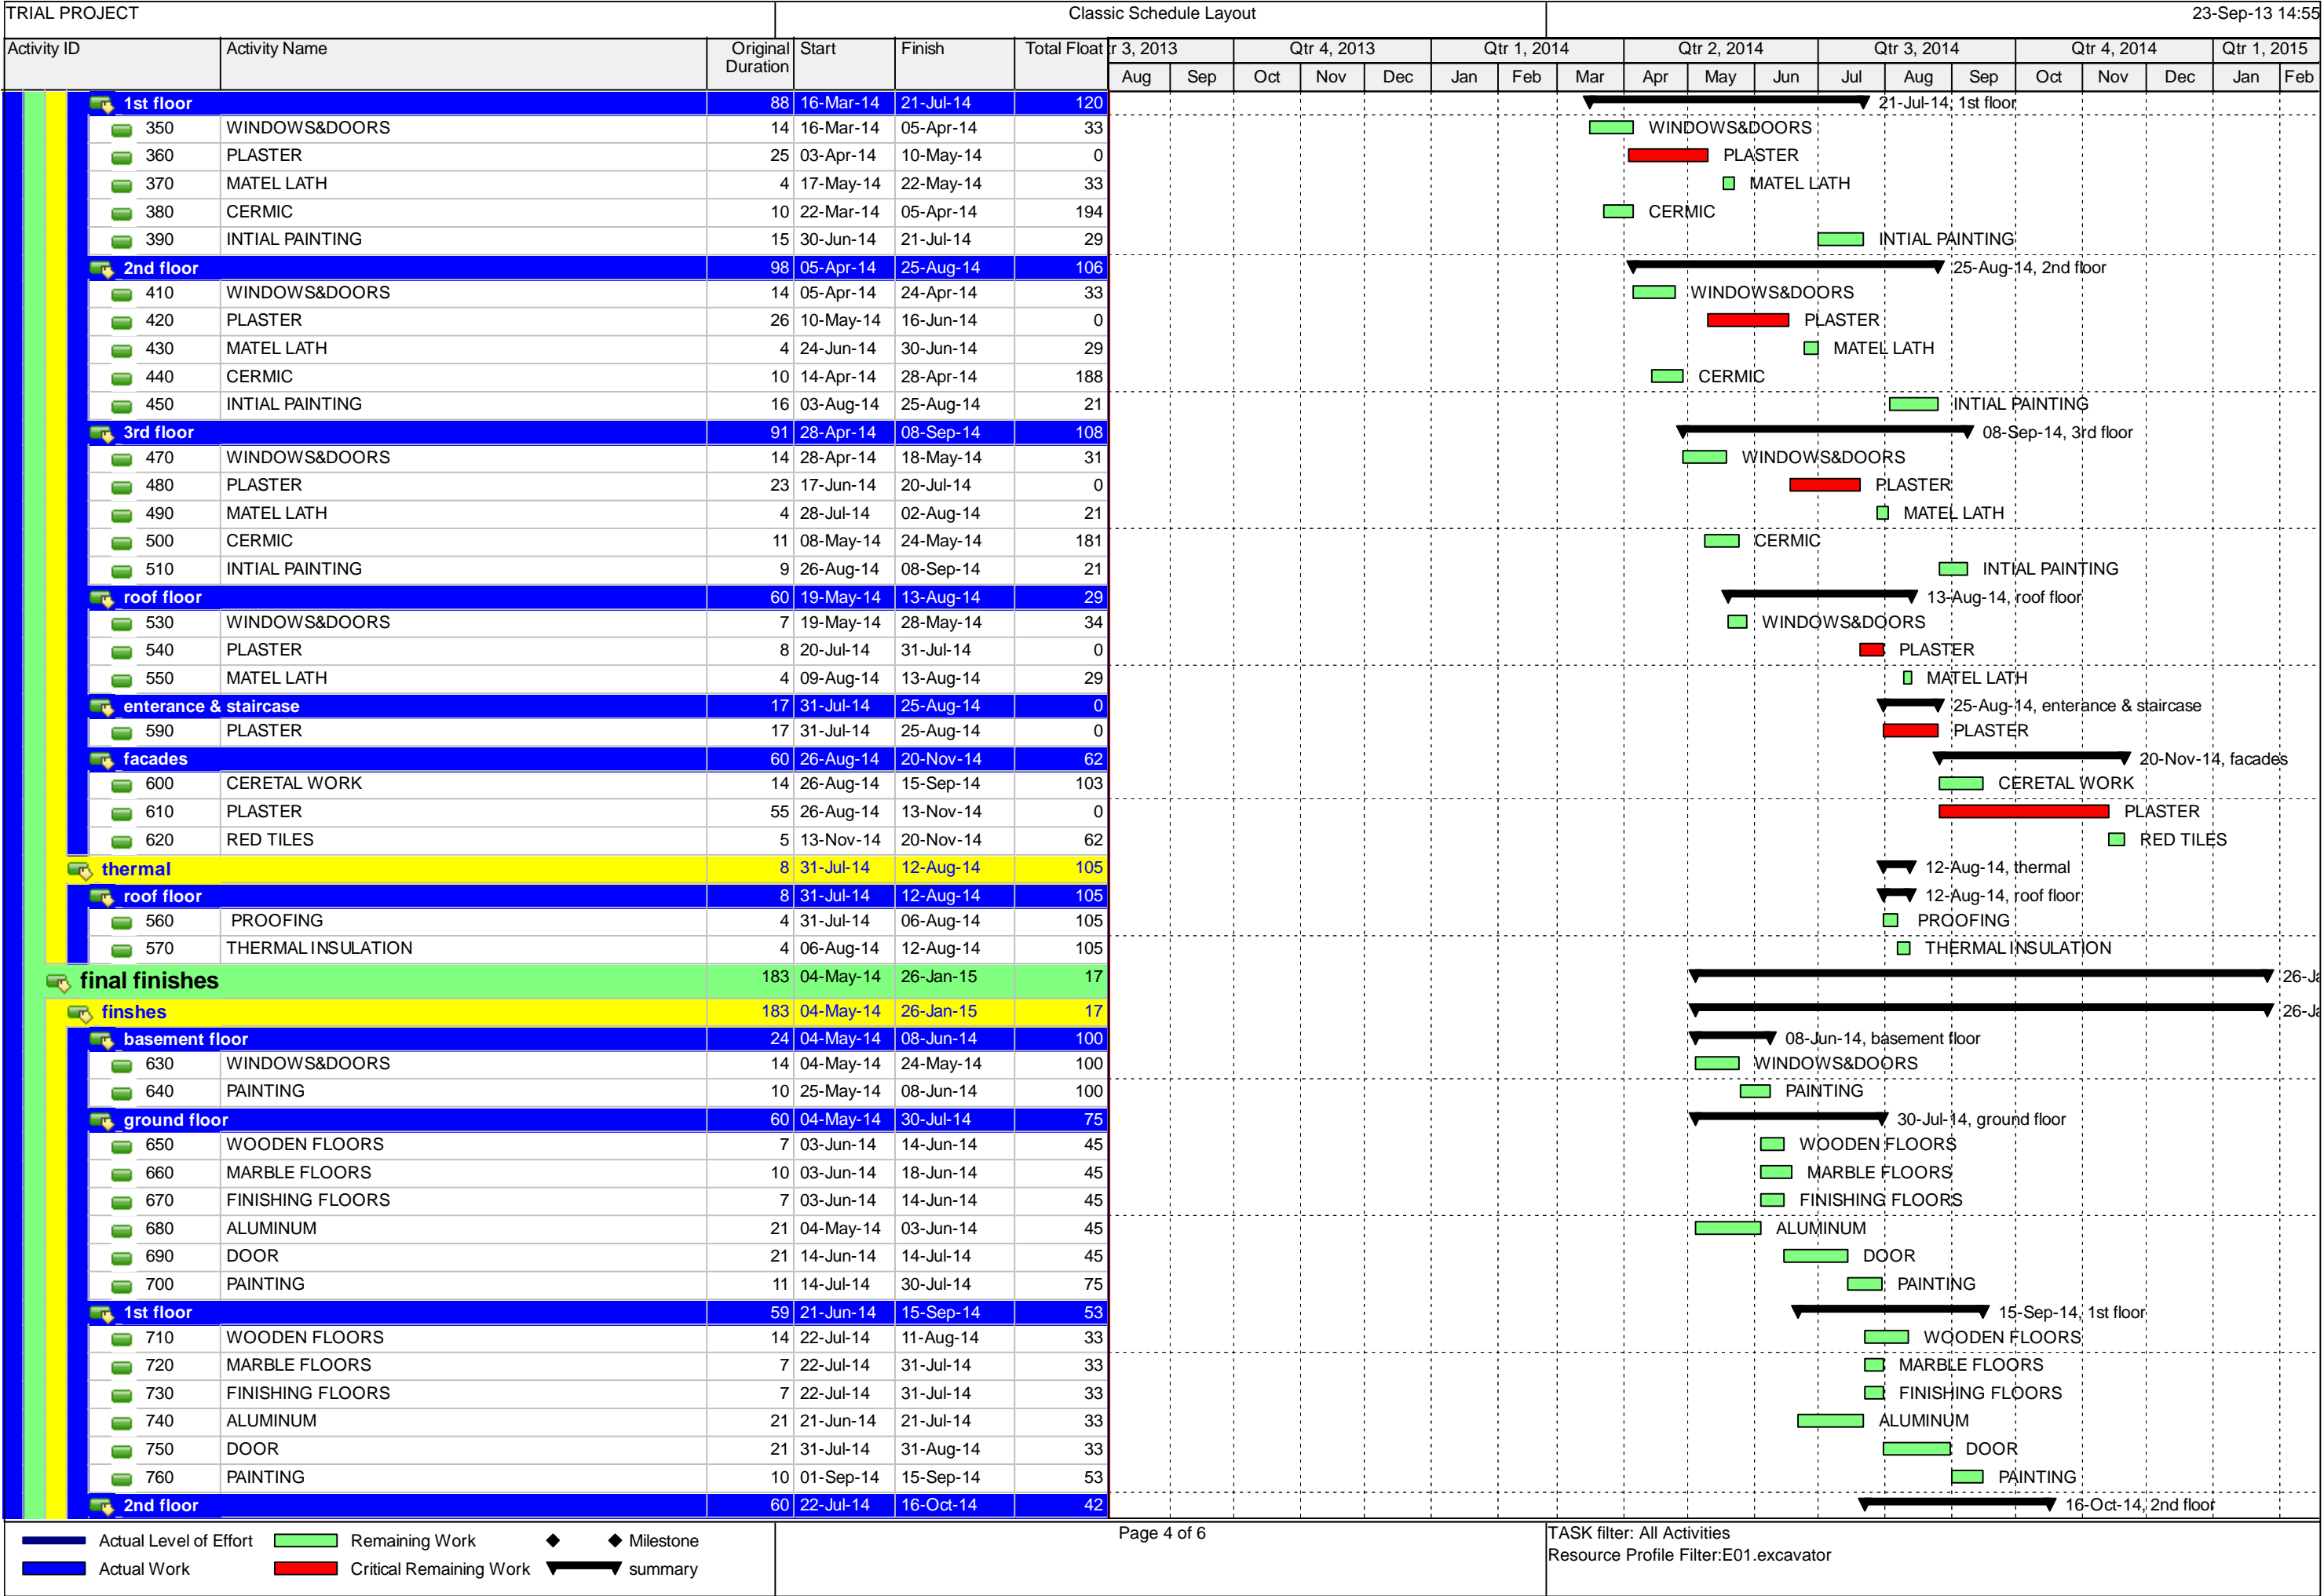

Activity ID		Activity Name	Original Duration	Start	Finish	Total Float	Qtr 3, 2013		Qtr 4, 2013		Qtr 1, 2014			Qtr 2, 2014			Qtr 3, 2014			Qtr 4, 2014			Qtr 1, 2015	
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
		<div></div> 770	WOODEN FLOORS	14	21-Aug-14	10-Sep-14	33																	
		<div></div> 780	MARBLE FLOORS	5	21-Aug-14	28-Aug-14	33																	
		<div></div> 790	FINISHING FLOORS	7	21-Aug-14	31-Aug-14	33																	
		<div></div> 800	ALUMINUM	21	22-Jul-14	21-Aug-14	33																	
		<div></div> 810	DOOR	21	01-Sep-14	01-Oct-14	33																	
		<div></div> 820	PAINTING	11	01-Oct-14	16-Oct-14	42																	
		<div></div> 3rd floor		58	08-Sep-14	01-Dec-14	21																	
		<div></div> 830	WOODEN FLOORS	14	08-Oct-14	28-Oct-14	21																	
		<div></div> 840	MARBLE FLOORS	5	08-Oct-14	15-Oct-14	21																	
		<div></div> 850	FINISHING FLOORS	7	08-Oct-14	19-Oct-14	21																	
		<div></div> 860	ALUMINUM	21	08-Sep-14	08-Oct-14	21																	
		<div></div> 870	DOOR	21	19-Oct-14	18-Nov-14	21																	
		<div></div> 880	PAINTING	9	18-Nov-14	01-Dec-14	21																	
		<div></div> roof floor		73	14-Aug-14	29-Nov-14	57																	
		<div></div> 890	CEMENT TILES	9	14-Aug-14	27-Aug-14	105																	
		<div></div> 900	FACADES PLASTER	9	27-Aug-14	09-Sep-14	105																	
		<div></div> 910	DOOR	7	18-Nov-14	29-Nov-14	57																	
		<div></div> entrance & staircase		48	26-Jul-14	04-Oct-14	71																	
		<div></div> 920	CERETAL WORK	21	26-Jul-14	25-Aug-14	0																	
		<div></div> 930	PLASTER COLORD	13	02-Sep-14	21-Sep-14	71																	
		<div></div> 940	MARBLE FLOORS	8	21-Sep-14	02-Oct-14	71																	
		<div></div> 950	MARBLE STAIRS	9	21-Sep-14	04-Oct-14	71																	
		<div></div> facades		45	22-Nov-14	26-Jan-15	0																	
		<div></div> 960	FACADES PLASTER DAHARA	40	22-Nov-14	18-Jan-15	0																	
		<div></div> 970	BARGOLAS	5	19-Jan-15	26-Jan-15	0																	
		<div></div> all floor		0	26-Jan-15	26-Jan-15	17																	
		<div></div> 1360	final fsihes closeout	0	26-Jan-15	26-Jan-15	17																	
		<div></div> mechincal works		81	03-Feb-14	01-Jun-14	181																	
		<div></div> mechincal		81	03-Feb-14	01-Jun-14	181																	
				<div></div> basement floor		15	03-Feb-14	24-Feb-14	233															
<div></div> 980	INTIAL SAINTARY WORK			7	03-Feb-14	12-Feb-14	0																	
<div></div> 990	FINAL SAINTARY WORK			3	20-Feb-14	24-Feb-14	233																	
<div></div> ground floor				16	16-Feb-14	11-Mar-14	226																	
<div></div> 1000	INTIAL SAINTARY WORK			7	16-Feb-14	25-Feb-14	5																	
<div></div> 1010	FINAL SAINTARY WORK			3	06-Mar-14	11-Mar-14	226																	
<div></div> 1st floor				20	11-Mar-14	09-Apr-14	209																	
<div></div> 1020	INTIAL SAINTARY WORK			7	11-Mar-14	20-Mar-14	9																	
<div></div> 1030	FINAL SAINTARY WORK			3	05-Apr-14	09-Apr-14	209																	
<div></div> 2nd floor				20	03-Apr-14	03-May-14	196																	
		<div></div> 1040	INTIAL SAINTARY WORK	7	03-Apr-14	13-Apr-14	18																	
		<div></div> 1050	FINAL SAINTARY WORK	3	28-Apr-14	03-May-14	196																	
		<div></div> 3rd floor		21	28-Apr-14	28-May-14	181																	
		<div></div> 1060	INTIAL SAINTARY WORK	7	28-Apr-14	08-May-14	27																	
		<div></div> 1070	FINAL SAINTARY WORK	3	25-May-14	28-May-14	181																	
		<div></div> roof floor		16	08-May-14	01-Jun-14	181																	
		<div></div> 1080	INTIAL SAINTARY WORK	3	08-May-14	12-May-14	47																	
		<div></div> 1090	FINAL SAINTARY WORK	2	28-May-14	01-Jun-14	181																	
		<div></div> all floor		0	01-Jun-14	01-Jun-14	181																	
		<div></div> 1370	mechincal closeout	0	01-Jun-14	01-Jun-14	181																	
<div></div> electrical work		241	23-Feb-14	09-Feb-15	0																			
<div></div> electrical		241	23-Feb-14	09-Feb-15	0																			
		<div></div> basement floor		79	23-Feb-14	18-Jun-14	105																	

